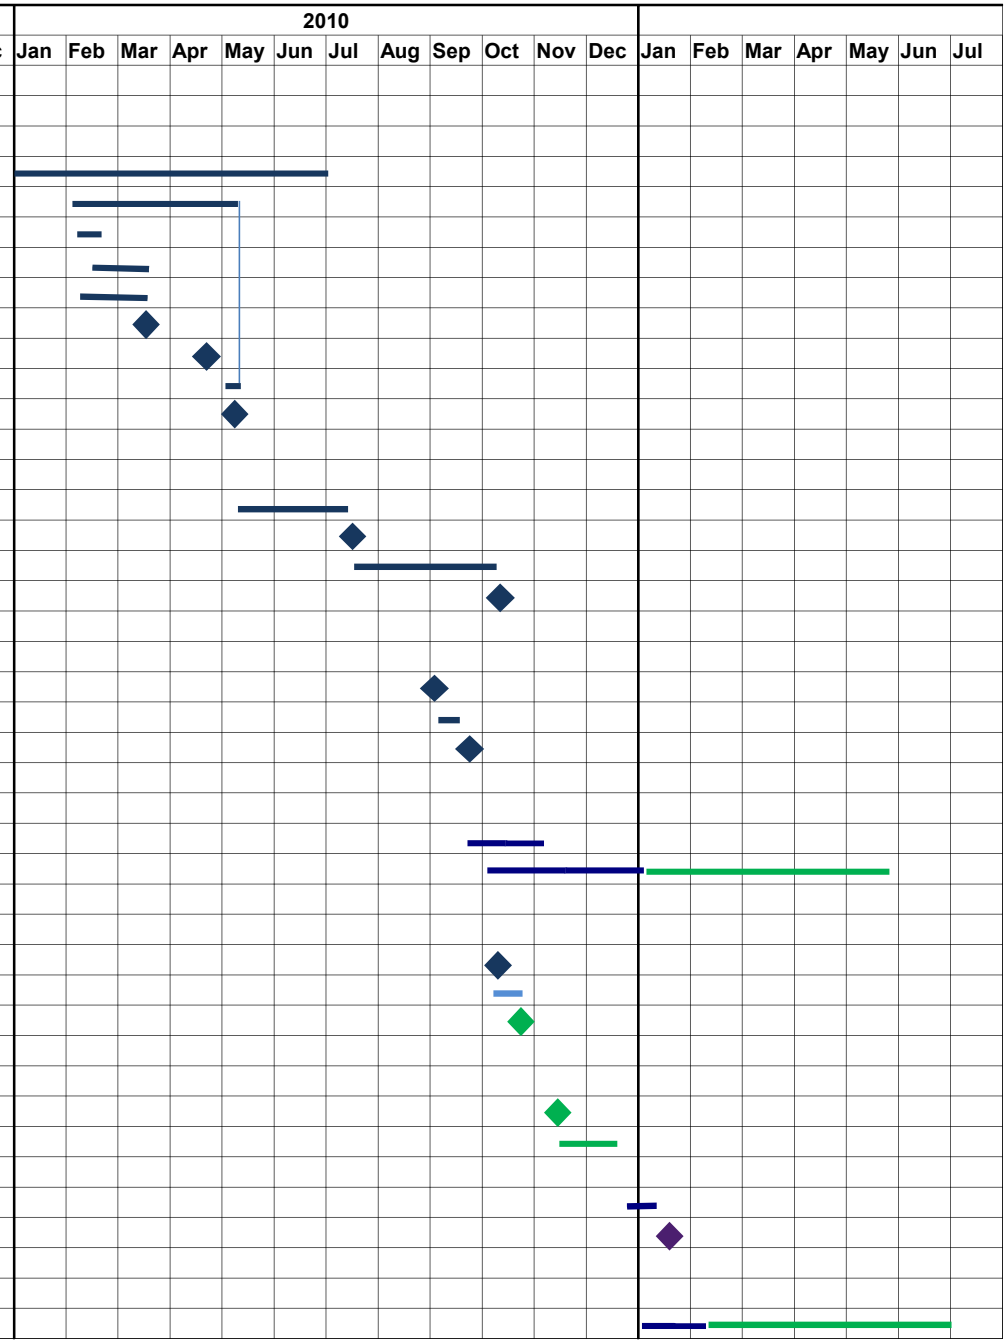Activity	Start	Finish
Decision Made to Buy House	1-Nov-09	1-Nov-09
Preparation and Land Purchase		
Alan Makes House Concept Drawings	1-Jan-10	1-Jul-10
Kanyhah in Thailand	7-Feb-10	8-May-10
Alex in Thailand	7-Feb-10	20-Feb-10
Purchase New Car in Bangkok	17-Feb-10	17-Mar-10
Looking for Land	8-Feb-10	19-Mar-10
Deposit and Contract for Land Purchase	19-Mar-10	19-Mar-10
Land Re-surveyed	22-Apr-10	22-Apr-10
Alan in Thailand	30-Apr-10	8-May-10
Land Purchase Completed	4-May-10	4-May-10
House Design by Architect		
Look for Architect		
Appointed Architect	14-Jul-10	14-Jul-10
Architects Detail Design	14-Jul-10	29-Sep-10
Final Construction Drawings received	10-Oct-10	10-Oct-10
Site Soil Investigation On Site		
Commissioned Site Soil Investigation	3-Sep-10	3-Sep-10
Site Soil Investigation On Site	8-Sep-10	10-Sep-10
Received Site Soil Investigation Report	22-Sep-10	22-Sep-10
Getting Quotations from Builders		
Kanyhah in Thailand	23-Sep-10	Ongoing
Getting Quotations from Builders	30-Sep-10	3-Jan-11
BOQ		
Commissioned QS to make BOQ	6-Oct-10	6-Oct-10
QS make BOQ	10-Oct-10	21-Oct-10
BOQ Received, Issued to Builders	21-Oct-10	21-Oct-10
Award Construction Contract		
Receive all Builders Quotations	18-Nov-10	18-Nov-10
Evaluate Quotations, Clarify with Builders	18-Nov-10	5-Jan-11
Select Builder		
Alan in Thailand	26-Dec-10	7-Jan-11
Award Construction Contract	2-Jan-11	2-Jan-11
House Build		
House Under Construction	6-Jan-11	14-Jun-11
